


Possession Type: A
Duration: 24 hours
Start Time: 0100 Sun
Finish Time: 0100 Mon

Week 09 - W/C: 26/05/2012

1. 2134 points – Install OLE mast bases.
2. 2143A points – Install S&C (Modular) on UCL + OLE bases.
3. Alexandra Palace – Construct new platforms and install OLE masts.
4. Register OLE to new portals.
5. USL – Install new OLE for lift for 2156A points.

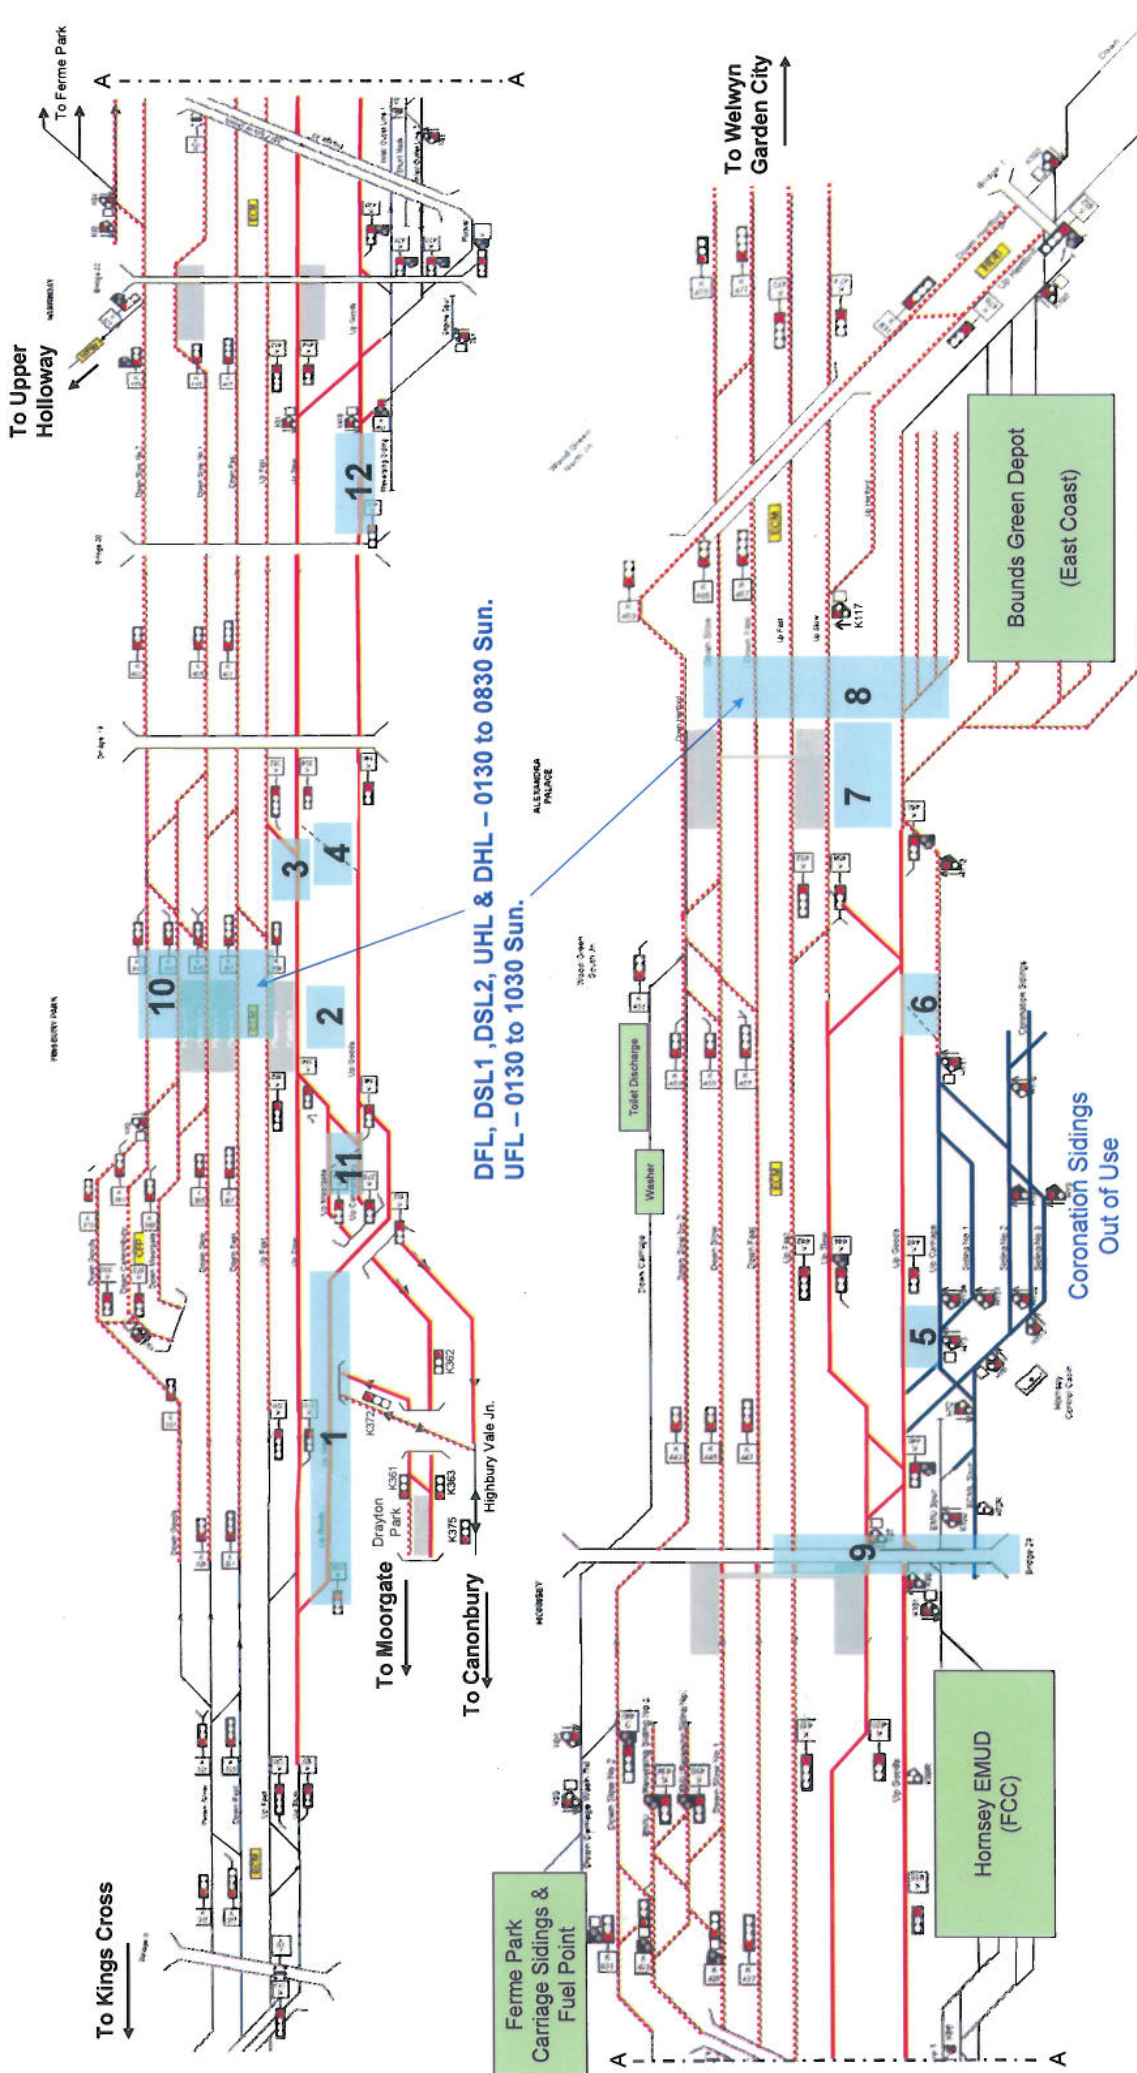


1. UGL – Follow-up tamp.
2. Platform 0 & -1 works.
3. UFL - 2098 points – Restress.
4. 2099 points – Install OLE through turnout.
5. 2134 points – Install OLE masts.
6. 2143B points – Install S&C (Modular) on UGL + mast bases.
7. Alexandra Palace – Construct new platforms.
8. Register OLE to new structures.
9. Hornsey Footbridge works (Thameslink Depot Works).
10. Platform 3 & 5 Extension – Install new decks to Bridge 16.
11. 2069 points – 6 week follow-up tamp.
12. UGL – 6 week follow-up tamp.

Possession Type: B + All Lines (0130 to 0830/1030 Sun)
Duration: 27 hours -Holloway to Wood Green South Jn.
 10 hours - Bounds Green Depot South End.
Start Time: 01.00 Sunday -Holloway to Wood Green South Jn.
 11.00 Sunday - Bounds Green Depot South End.
Finish Time: 21.00 Sunday - Bounds Green Depot South End.
 04.00 Monday -Holloway to Wood Green South Jn.


Week 10 (Jubilee BH) - W/C: 02/06/2012


1. K2099 points out of use until week 13.

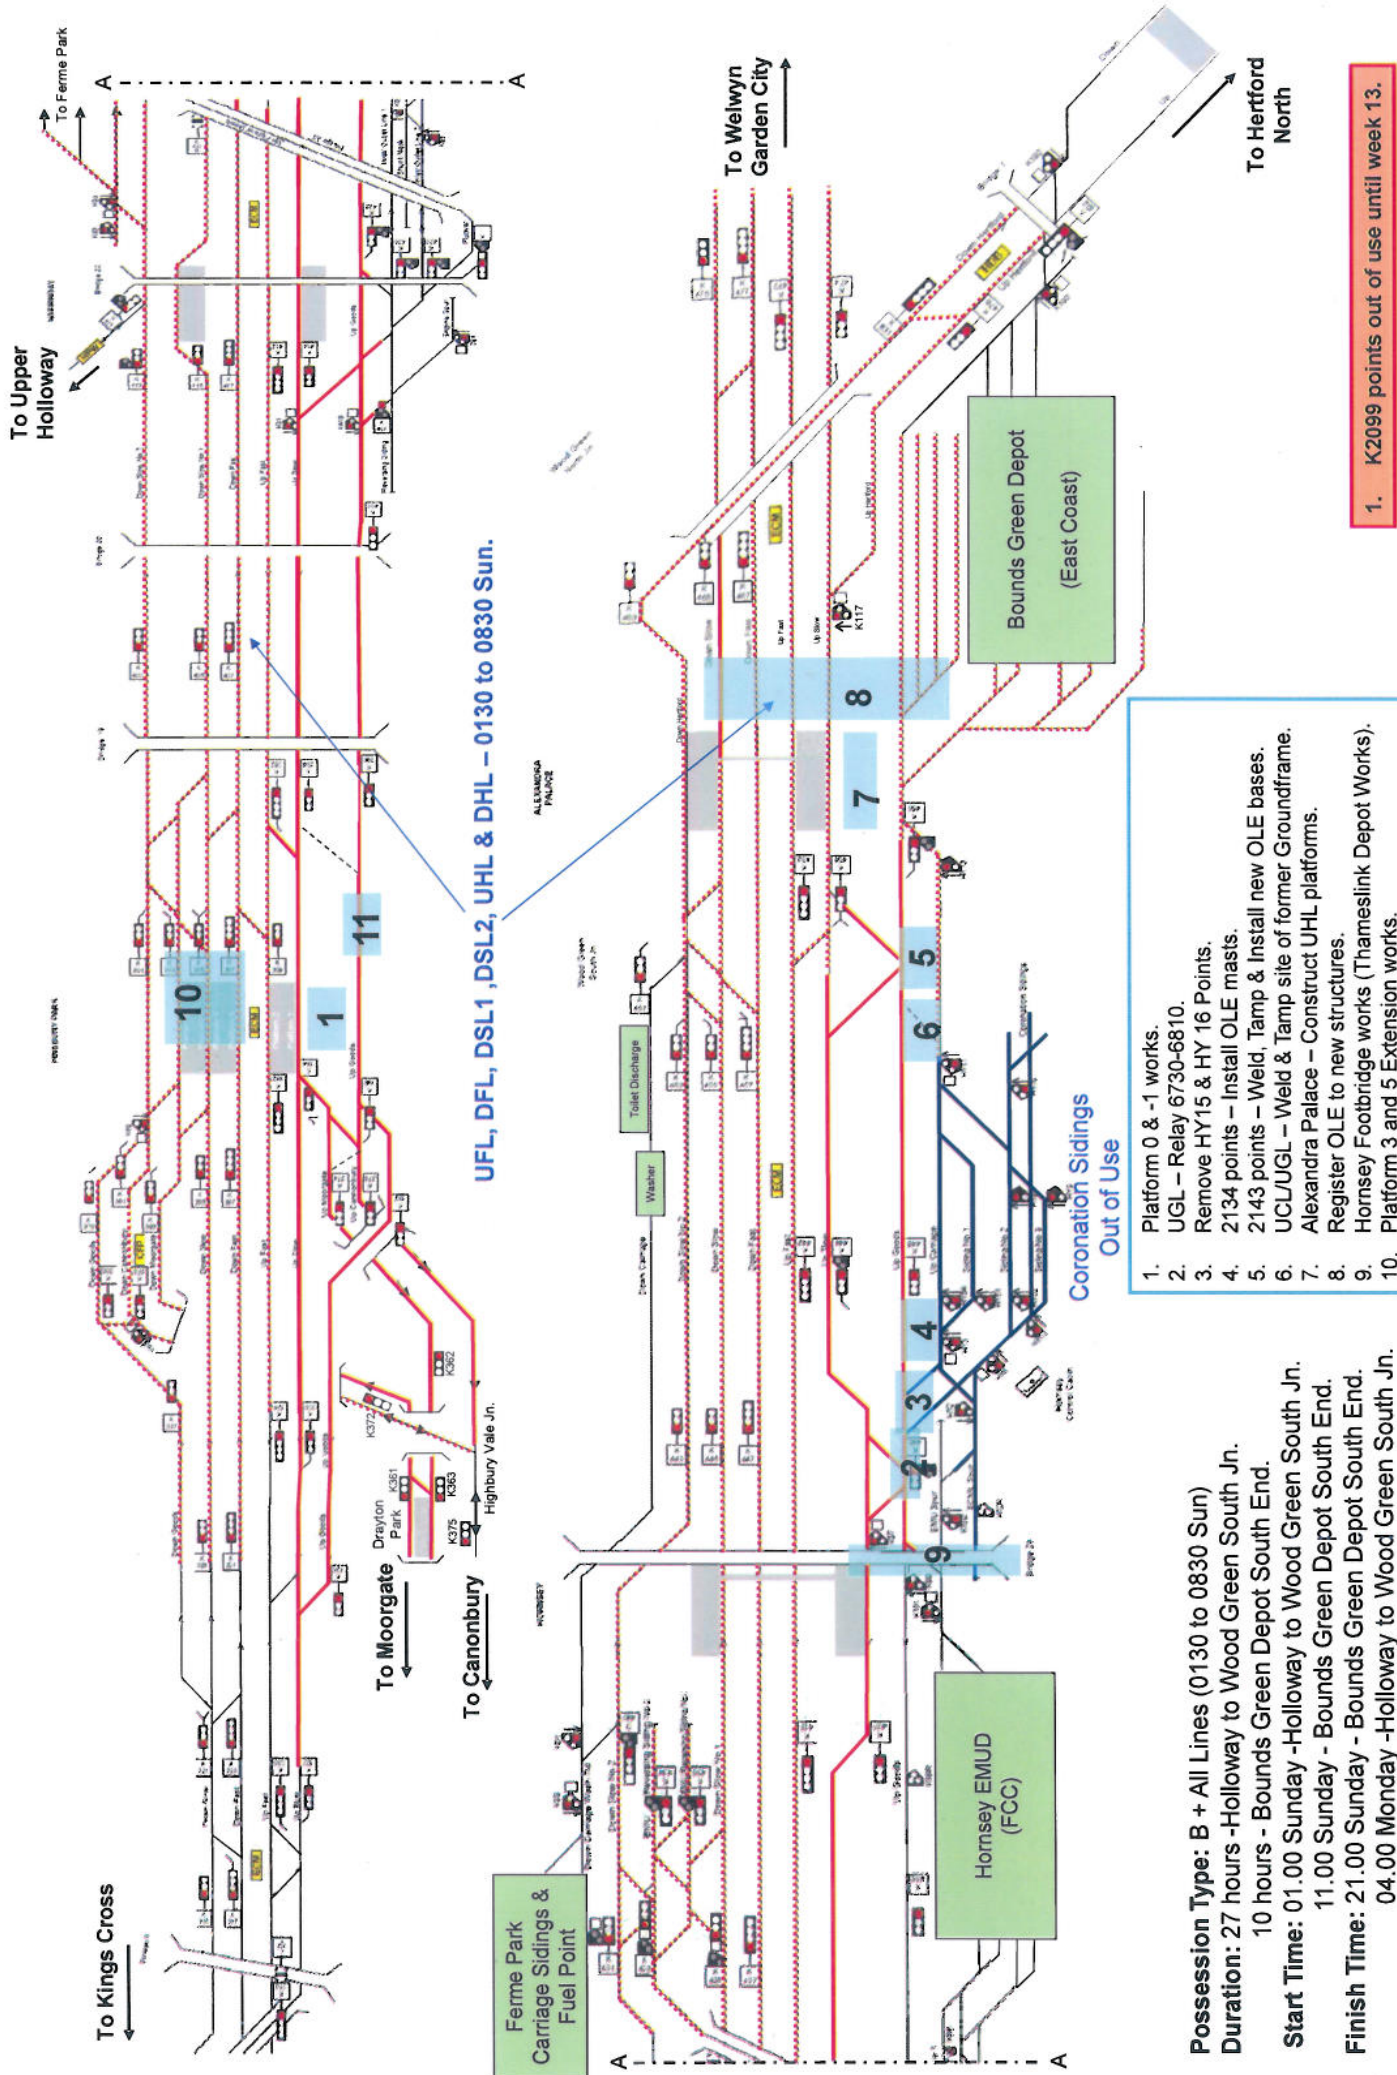

Possession Type: B + All Lines (0130 to 0830 Sun)
Duration: 27 hours -Holloway to Wood Green South Jn.
 10 hours - Bounds Green Depot South End.
Start Time: 01.00 Sunday -Holloway to Wood Green South Jn.
 11.00 Sunday - Bounds Green Depot South End.
Finish Time: 21.00 Sunday - Bounds Green Depot South End.
 04.00 Monday -Holloway to Wood Green South Jn.

1. Platform 0 & -1 works.
2. UGL - Relay 6730-6810.
3. Remove HY15 & HY 16 Points.
4. 2134 points - Install OLE masts.
5. 2143 points - Weld, Tamp & Install new OLE bases.
6. UCL/UGL - Weld & Tamp site of former Groundframe.
7. Alexandra Palace - Construct UHL platforms.
8. Register OLE to new structures.
9. Hornsey Footbridge works (Thameslink Depot Works).
10. Platform 3 and 5 Extension works.
11. UGL - 6 week follow-up tamp.

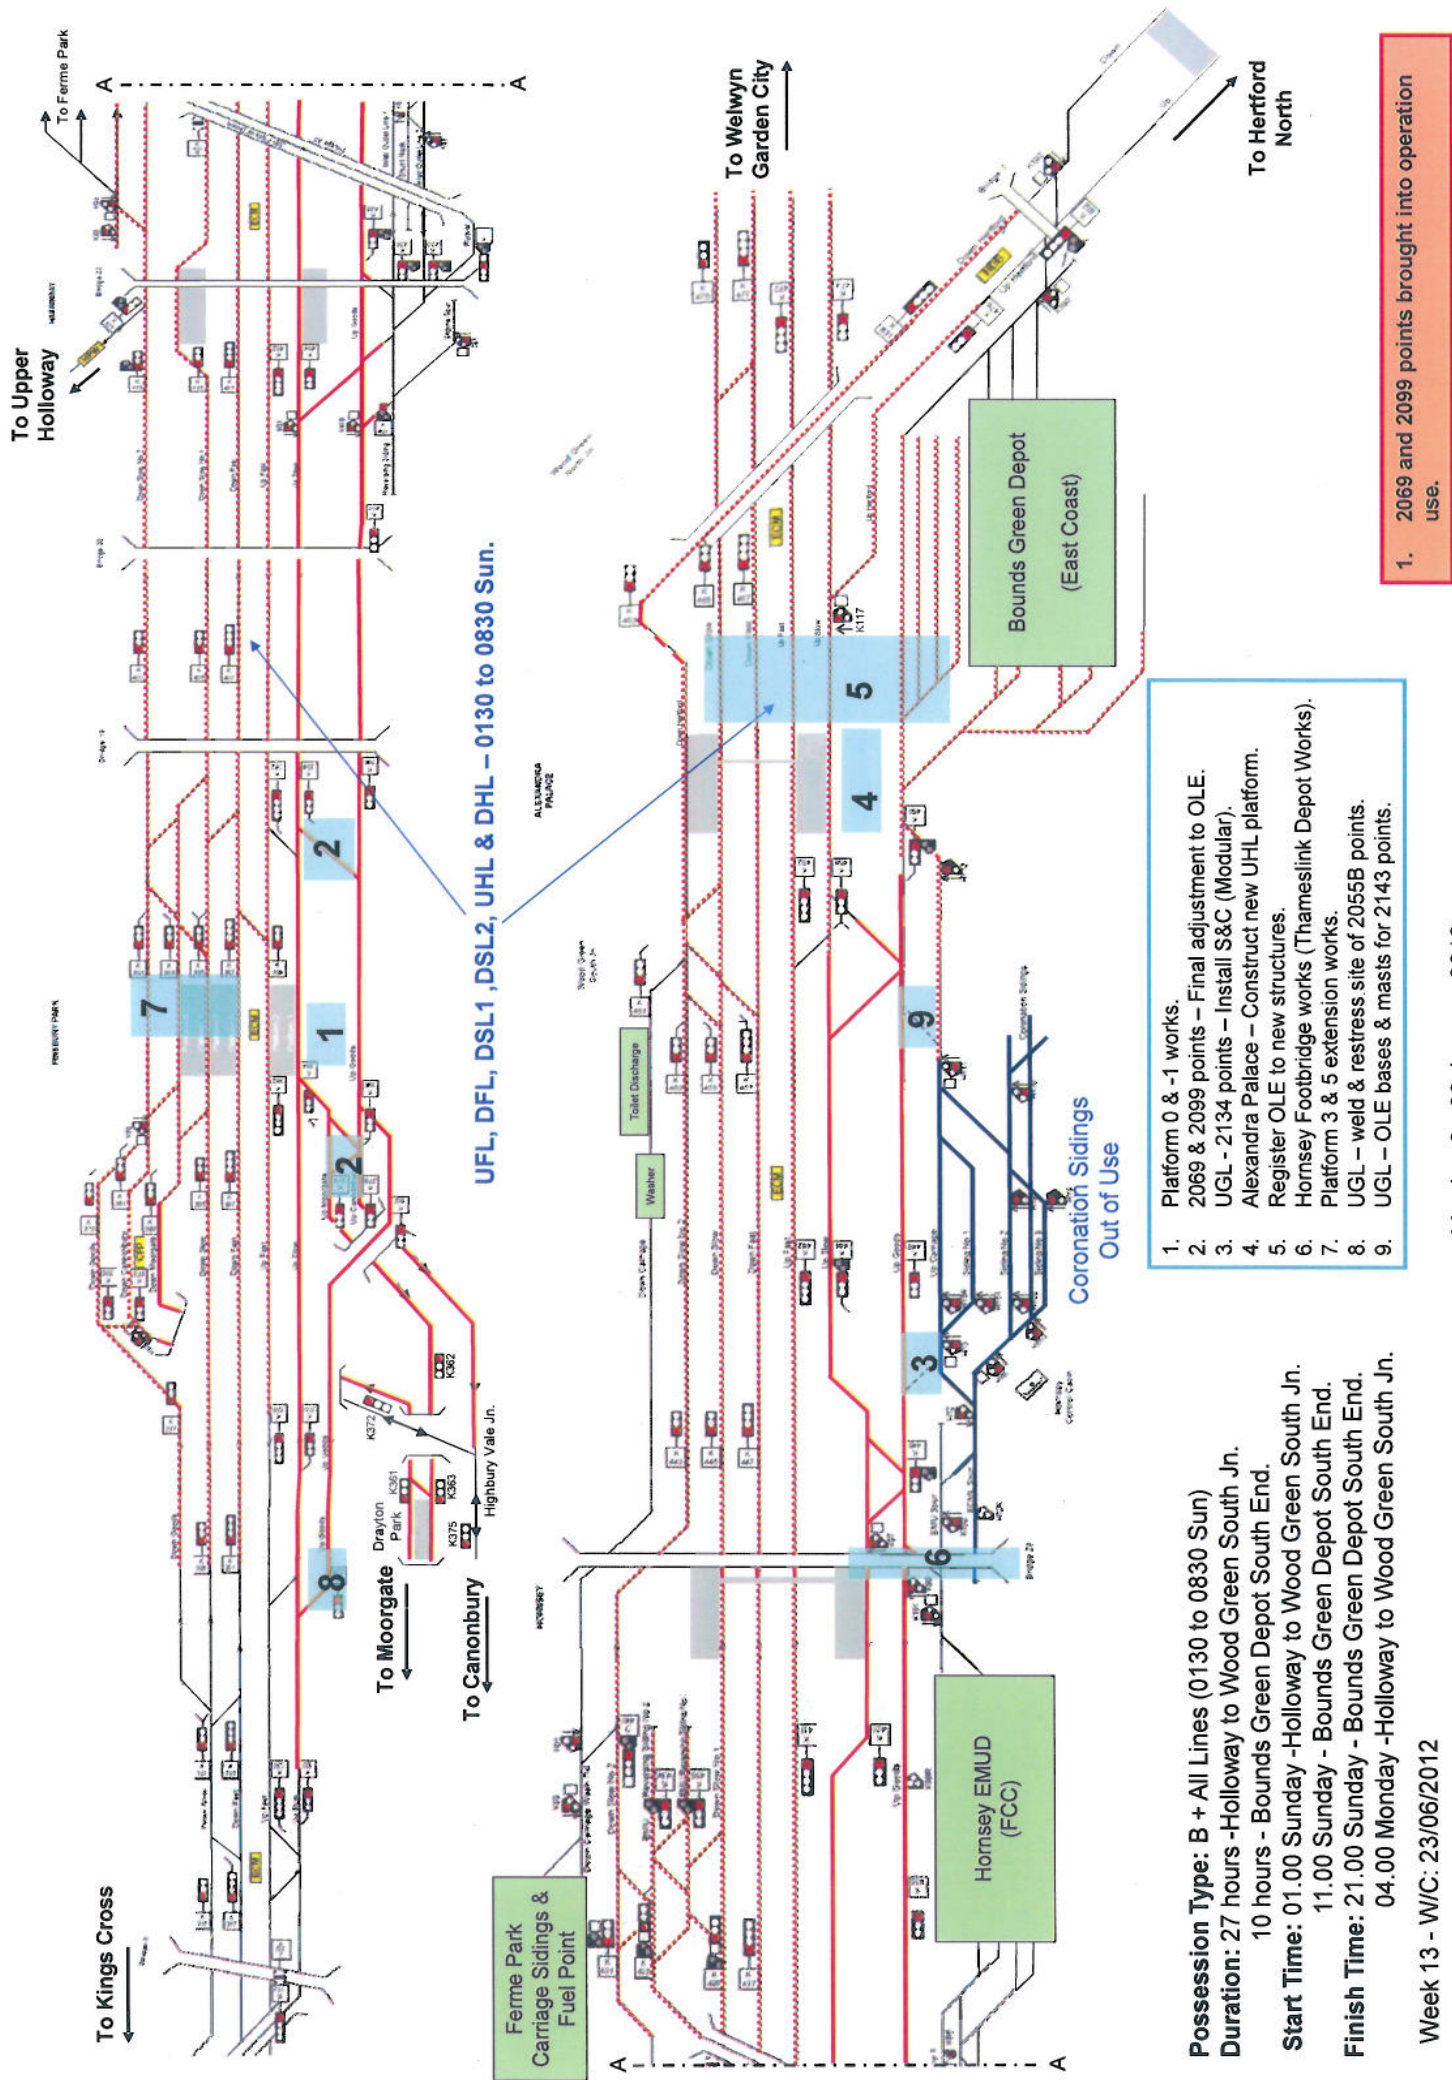


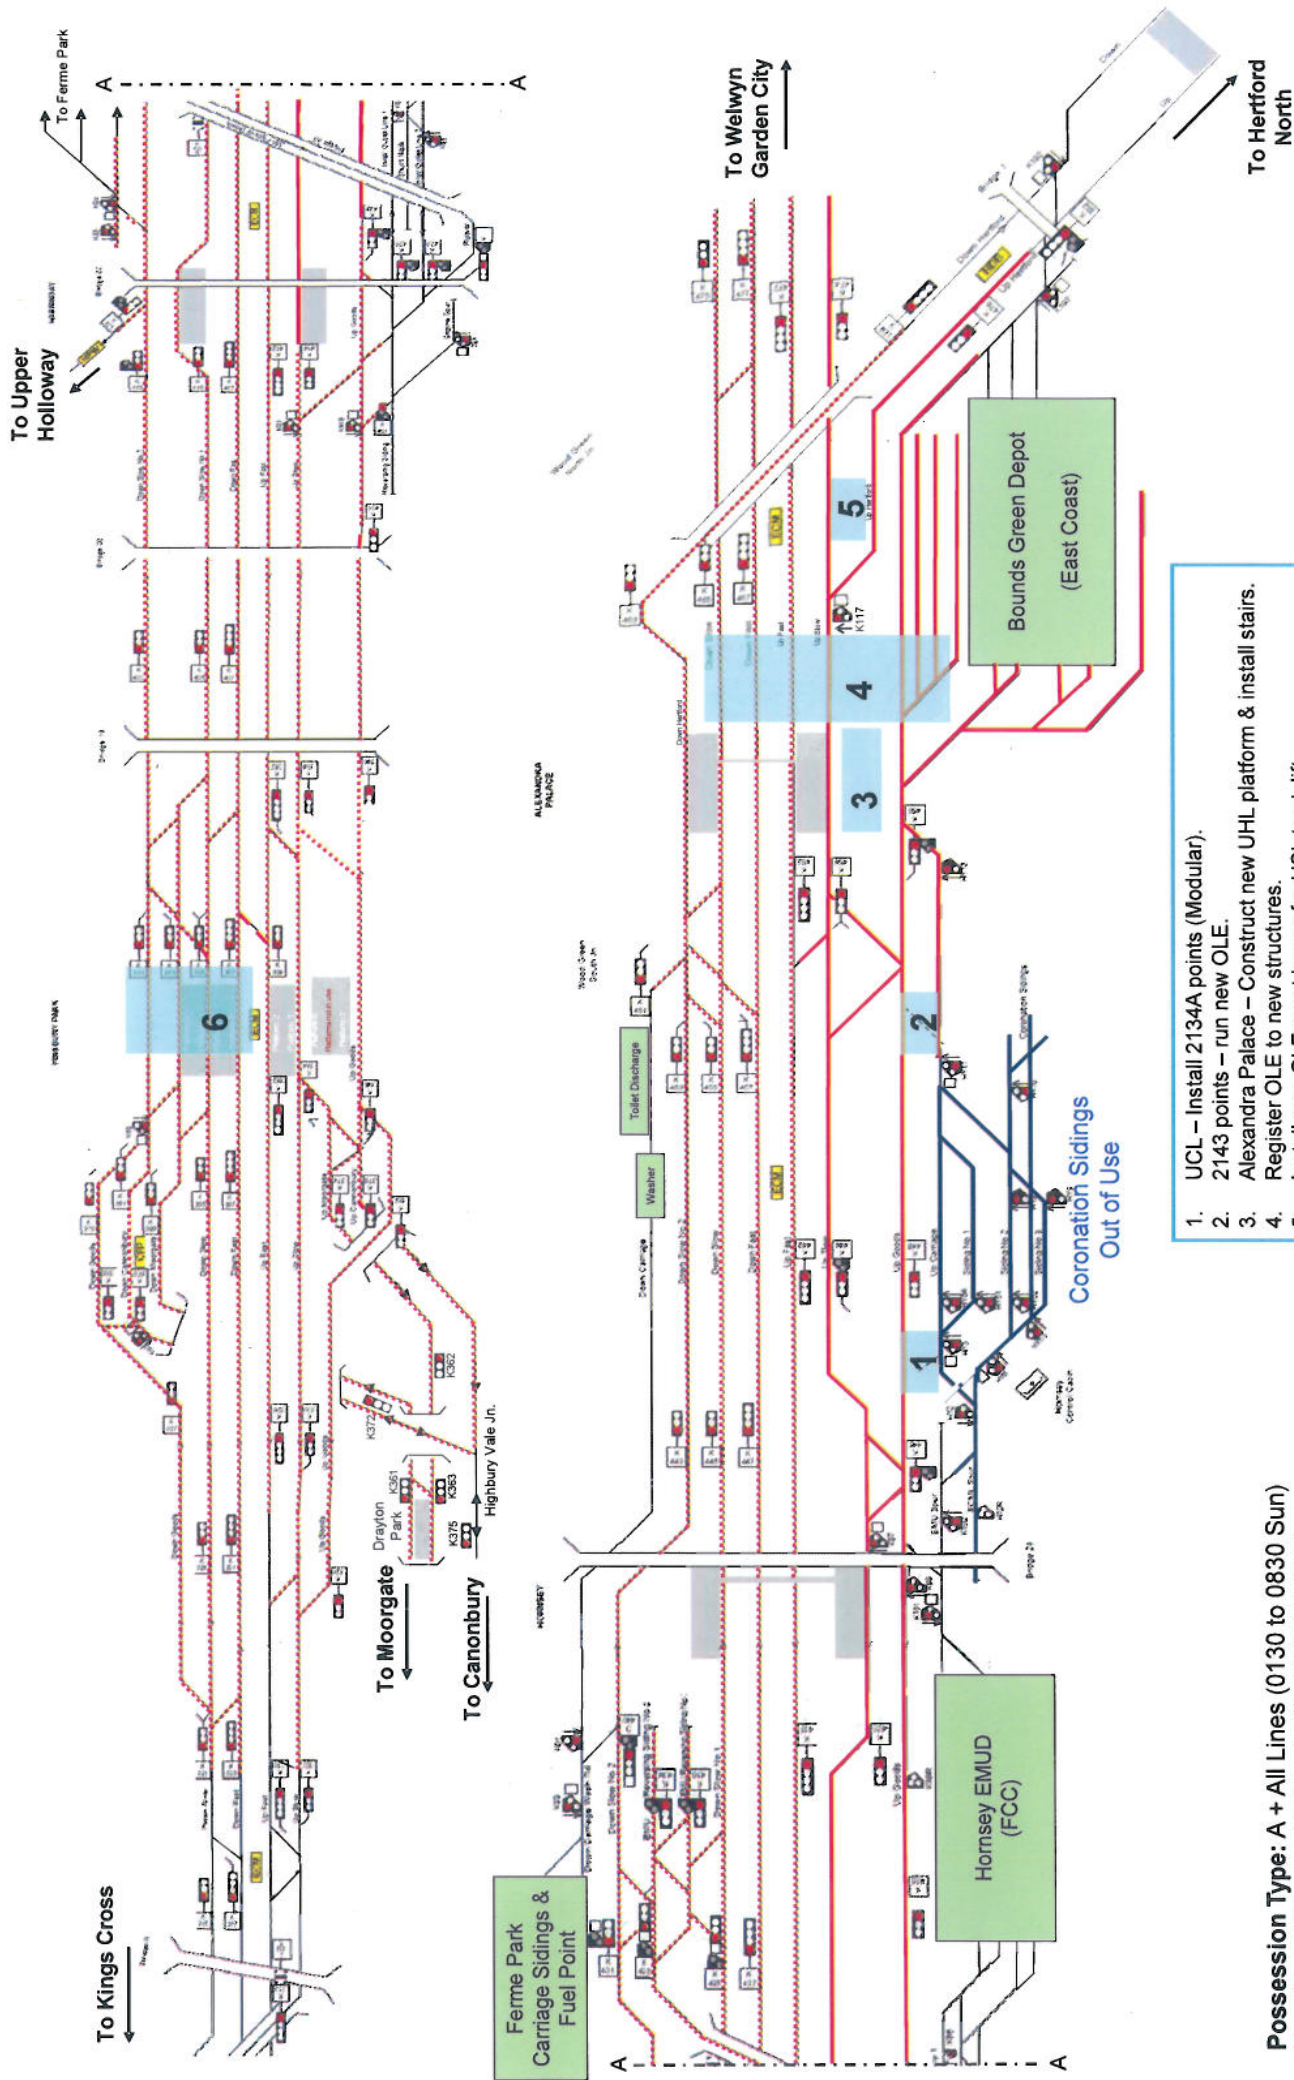

Possession Type: A + All Lines (0130 to 0830 Sun)
Duration: 24 hours (C Short 0120 to 2000 Sun)
Start Time: 0100 Sun (0120 C Short)
Finish Time: 0100 Mon (2000 Sun C Short)


Week 14 - W/C: 30/06/2012

Version 8 - 30 January 2012

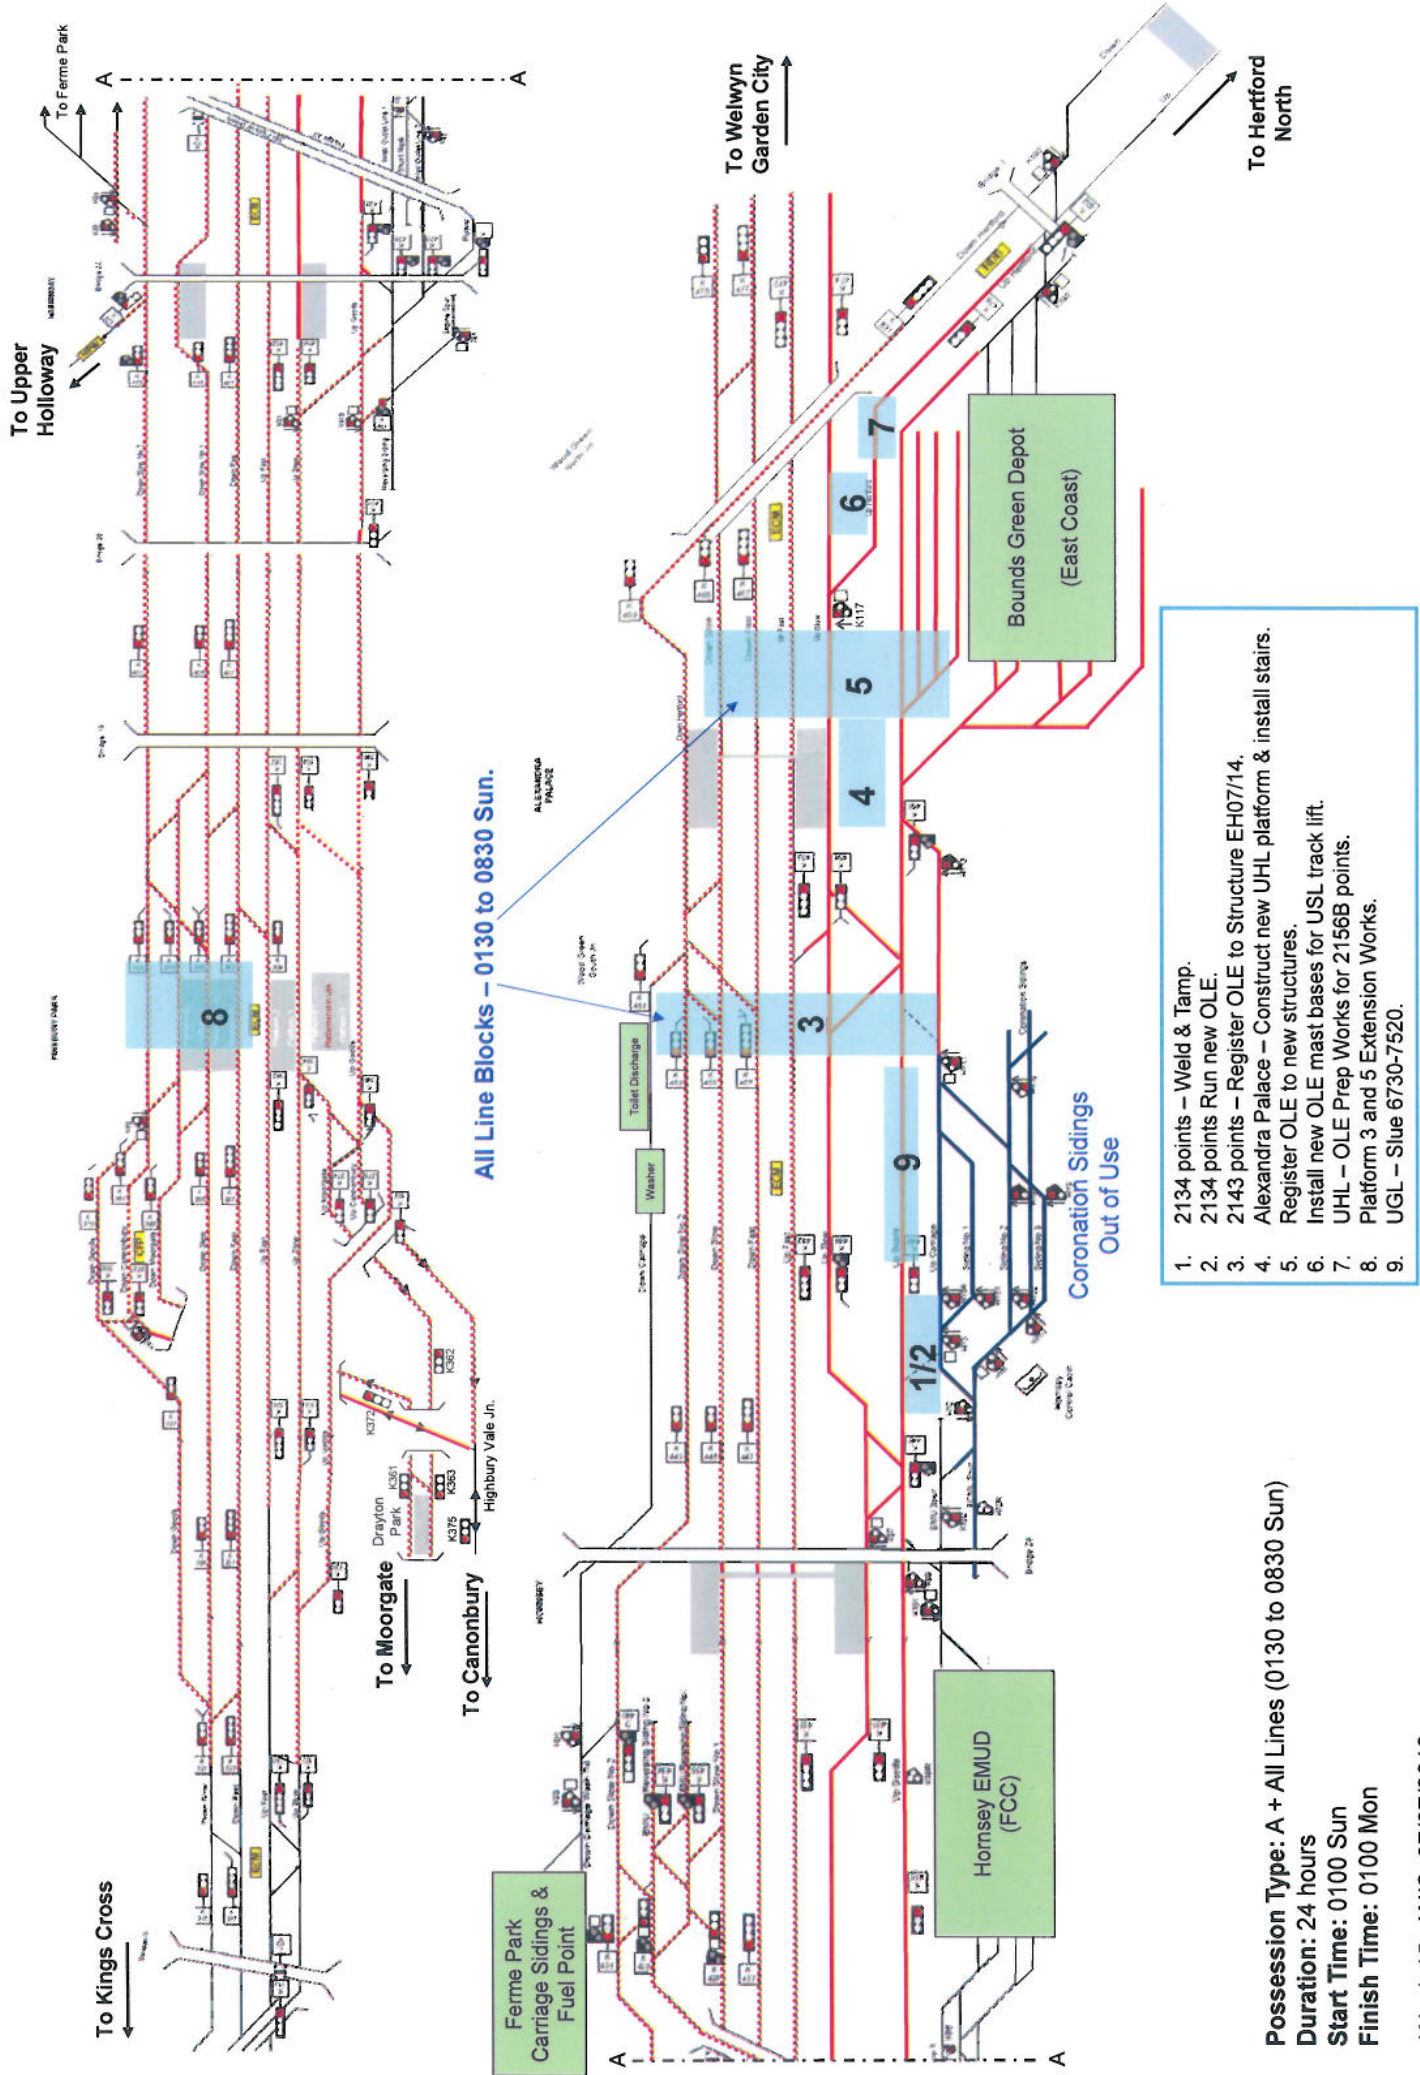

1. 2134 points - Weld & Tamp.
2. 2134 points Run new OLE.
3. 2143 points - Register OLE to Structure EH07/14.
4. Alexandra Palace - Construct new UHL platform & install stairs.
5. Register OLE to new structures.
6. Install new OLE mast bases for UHL track lift.
7. UHL - OLE Prep Works for 2156B points.
8. Platform 3 and 5 Extension Works.
9. UGL - Slue 6730-7520.

Possession Type: A + All Lines (0130 to 0830 Sun)
Duration: 24 hours
Start Time: 0100 Sun
Finish Time: 0100 Mon
Week 15 - W/C: 07/07/2012

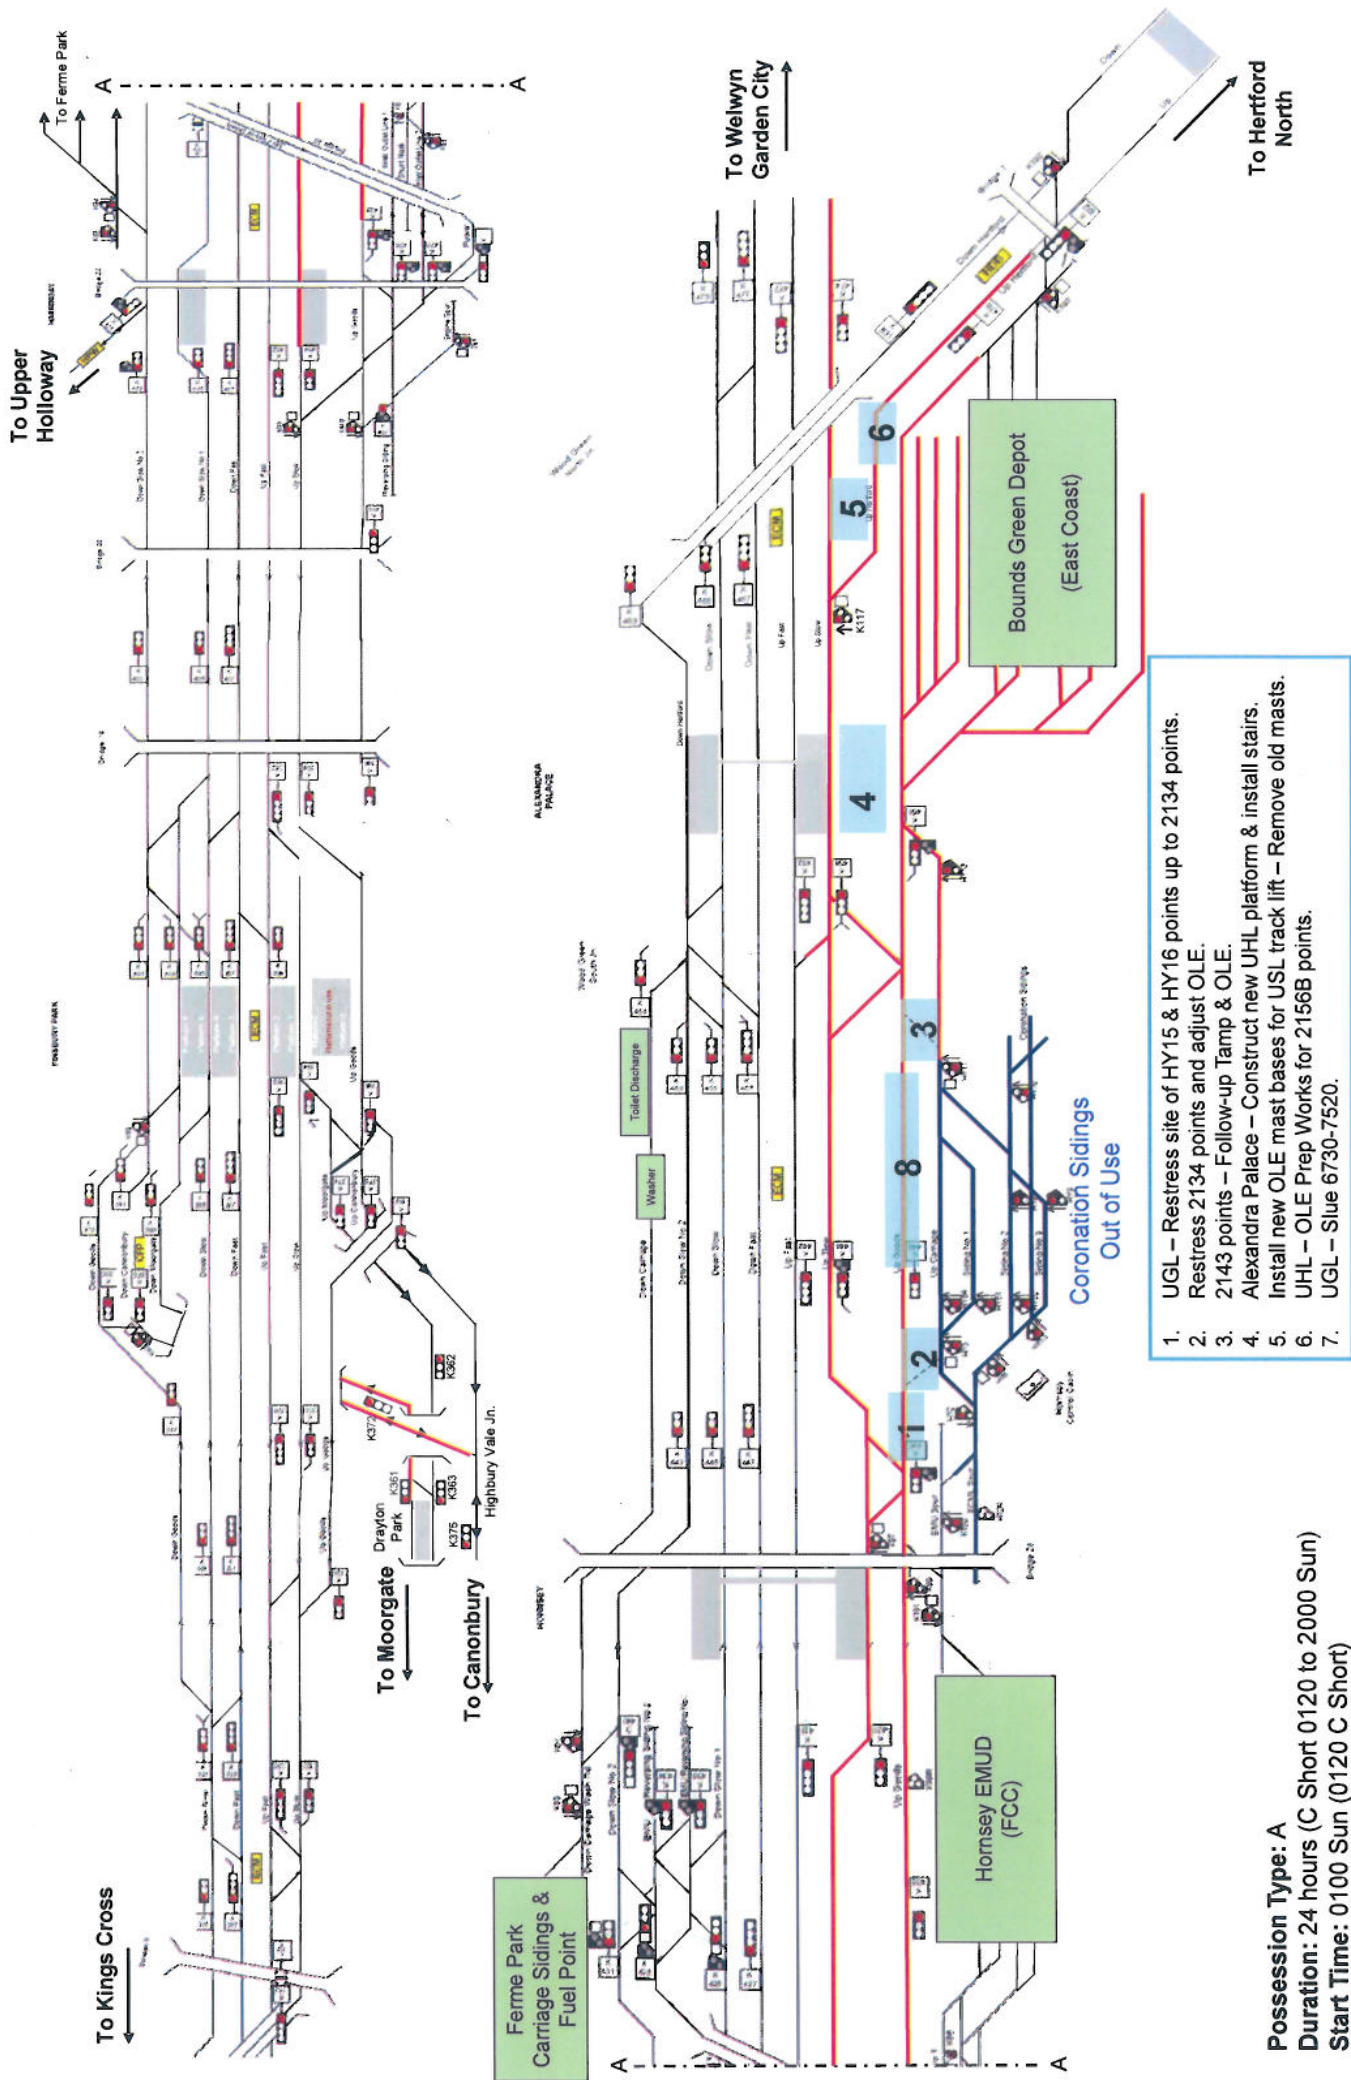

Possession Type: A
Duration: 24 hours (C Short 0120 to 2000 Sun)
Start Time: 0100 Sun (0120 C Short)
Finish Time: 0100 Mon (2000 Sun C Short)

Week 16 - W/C: 14/07/2012

Version 8 - 30 January 2012
